


Sprint 1 Review

Implemented features/completed work + design decisions (narrative)

- Installation of software necessities (installed and configured by all team members)
- Mockups
- API tests
- GitHub repo
- Backlog and estimates
- Technical feasibility

Burndown chart

Burndown chart - Sprint 1

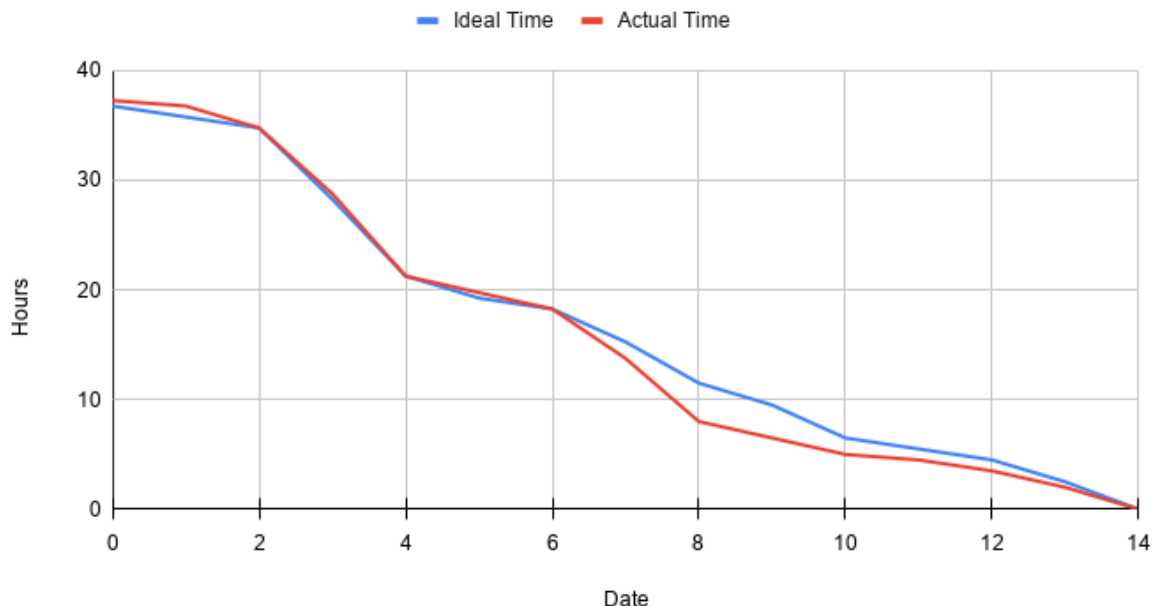

We maintained a consistent pace with our tasks, with better time management and improved task completion speed by the second week. By the end of the sprint we managed to finish all the tasks we set out to complete faster than the time we originally estimated it would take.

Sprint review

The main objectives for this sprint was to set up the necessary software for the project, research competitors for ideas on web design, set up the organisational structure for the sprint (including the sprint and product backlog, burndown charts and user stories), perform interviews to define the user stories of the project, create mockups of the preliminary web design our team envisioned as the final product, and begin to implement and test some web scraping capabilities. Our team managed to achieve all of the tasks in the sprint backlog that we set out to do, and in less time than we originally thought. We worked efficiently, however

communication could have been clearer and more consistent. Once we realised this though, we made sure to be clearer about our individual progress so that everyone was on the same page. We began to implement web scraping, but mostly in a testing capacity, and the full scale scraping will be moved to the next sprint.

Sprint retrospective

Overall this first sprint went well and we made strong progress over the two week period. We divided the tasks clearly at the start of the sprint and everyone completed their respective tasks on time. There was a positive collaborative effort from each team member, and we were able to complete all the tasks we set out to do without any major issues.

One area we identified for improvement is communication around the completion of tasks. On a few occasions there were tasks that had been completed but other team members were not notified until the next group meeting. While not a serious issue, it ran the risk of another team member duplicating the work which is not a productive way of doing things moving onto more complex sprint tasks. After recognising this though we course corrected and then communication noticeably improved by the second half of the sprint. The updates were more consistent and everyone was on the same page.

Going into the next sprints, our team would like to maintain consistent communication by providing updates in our group chat about which tasks are completed, and updating the sprint backlog sheet in real time. This will enable us to have transparency about the work of each team member, while keeping us aligned with the goals we set for ourselves. Overall there has been a positive team dynamic, and we successfully completed all the tasks we set out to do.
